




WAKEFIELD PUBLIC SAFETY PROJECT WEEKLY UPDATE

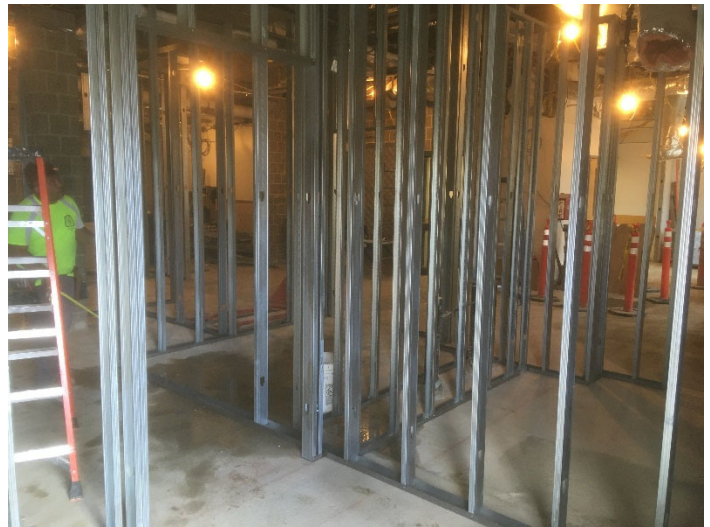

THIS WEEK'S PROGRESS:

(June 6 – June 10, 2022)

- Continue installation/drilling of micro-piles for building addition
- Begin rough electrical in lobby & dispatch
- Place concrete at new lobby vestibule
- Begin interior framing of metal stud walls at new Lobby, Dispatch Room, and adjacent spaces
- Begin rough plumbing for new Lobby and Restrooms
- Cut & cap fire sprinkler lines in vehicle garage for new Dispatch area

PROJECT TRACKING: Phase 1:

- Approx. 45% complete

ANTICIPATED NEXT WEEK:

(June 13 – June 17, 2022)

- Continue interior framing
- Continue rough electrical
- Continue rough plumbing
- Complete installation/drilling of micro-piles for building addition
- Begin erection of steel at new Lobby Vestibule
- Frame old entryway to receive masonry
- Install HVAC ductwork in new Lobby area

MILESTONE DATES:

- Micro-piles for building addition complete before mid-June.
- Structural steel for new entrance vestibule starting mid-June.

For more information on the project:

<https://wakefieldpublicsafetyproject.com/>
